BRUHAT BANGALORE MAHANAGARA PALIKE

Name of Work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No 15..

Dasarahalli Division

MEASURMENT BOOK

PAYMENT CERTIFICATE

First & Final BILL

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No 15..

Measurement Sheet

First and Final

Item No:	1
Item Name:	Removing and refixing stone slabs of drains and pointing in CM (1:3) ,SR Rate 2018-19. P27,I 5.33

	CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
	Bharathi Theater(W0223)								
	0-30	1	30.00			0.90		27.00	
	30-60	1	30.00			0.90		27.00	
	60-90	1	30.00			0.90		27.00	
	90-110	1	20.00			0.90		18.00	
	Excel kalyana mantapa(W0225)								
	0-30	1	30.00			0.90		27.00	
	30-60	1	30.00			0.90		27.00	
	60-90	1	30.00			0.90		27.00	
	90-120	1	30.00			0.90		27.00	
	120-138	1	18.00			0.90		16.20	
	1st cross(W0214)								
	0-30	2	30.00			0.90		54.00	
	30-60	2	30.00			0.90		54.00	
	60-85	2	25.00			0.90		45.00	
	2nd cross((W0212)								
	0-30	2	30.00			0.90		54.00	
	30-60	2	30.00			0.90		54.00	
	60-90	2	30.00			0.90		54.00	
	90-116	2	26.00			0.90		46.80	
	cross(W0227)								
	0-30	2	30.00			0.90		54.00	
	30-36	2	6.00			0.90		10.80	
	cross(W0229)								
	0-30	2	30.00			0.90		54.00	
	30-38	2	8.00			0.90		14.40	
								718.20	**Sqm**
	missing slab							**460.00**	
						Total Qty Work Done		**258.20**	**Sqm**
						Qty Payable in this bill		**258.20**	**Sqm**

Contractor Representative

Assistant Engineer

15/11

Asst.Executive Engineer

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಜಿ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿ...
ಬಾ...ಗುಂಟೆ.

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No 15..

Measurement Sheet

First and Final

Item No:	2
Item Name:	KSRRB 300 - Excavation for road, drains and similar works SRRB 300-1. Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto .imeters and an erage lift upto 0.5 m, exf-avated surface leveled and sides neatly dressed, the disposed earth to be leveled neatly after breaking of clods complete as perspecifications. MORTH / Chapter SR Rate.2018-19.p158/i21.3

CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	1	30.00			0.90	1.20	32.40	
30-60	1	30.00			0.90	1.20	32.40	
60-90	1	30.00			0.90	1.20	32.40	
90-110	1	20.00			0.90	1.20	21.60	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			0.90	1.20	32.40	
30-60	1	30.00			0.90	1.20	32.40	
60-90	1	30.00			0.90	1.20	32.40	
90-120	1	30.00			0.90	1.20	32.40	
120-138	1	18.00			0.90	1.20	19.44	
1st cross(W0214)								
0-30	2	30.00			0.90	0.90	48.60	
30-60	2	30.00			0.90	0.90	48.60	
60-85	2	25.00			0.90	0.90	40.50	
2nd cross((W0212)								
0-30	2	30.00			0.90	0.90	48.60	
30-60	2	30.00			0.90	0.90	48.60	
60-90	2	30.00			0.90	0.90	48.60	
90-116	2	26.00			0.90	0.90	42.12	
cross(W0227)								
0-30	2	30.00			0.90	0.90	48.60	
30-36	2	6.00			0.90	0.90	9.72	
cross(W0229)								
0-30	2	30.00			0.90	0.90	48.60	
30-38	2	8.00			0.90	0.90	12.96	
road side and kerb								
Bharathi Theater(W0223)								
0-30	1	30.00			0.80	0.30	7.20	
30-60	1	30.00			0.80	0.30	7.20	
60-90	1	30.00			0.80	0.30	7.20	
90-110	1	20.00			0.80	0.30	4.80	
Excel kalyana mantapa(W0225)								

Scanned with CamScanner

	CHAINAGE	NO	L	B	B1	Avg B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)	(m)	(m)		
	0-30	1	30.00			0.80	0.30	7.20	
	30-60	1	30.00			0.80	0.30	7.20	
	60-90	1	30.00			0.80	0.30	7.20	
	90-120	1	30.00			0.80	0.30	7.20	
	120-138	1	18.00			0.80	0.30	4.32	
	1st cross(W0214)								
	0-30	1	30.00			0.80	0.30	7.20	
	30-60	1	30.00			0.80	0.30	7.20	
	60-85	1	25.00			0.80	0.30	6.00	
	2nd cross((W0212)								
	0-30	2	30.00			0.80	0.30	14.40	
	30-60	2	30.00			0.80	0.30	14.40	
	60-90	2	30.00			0.80	0.30	14.40	
	90-116	2	26.00			0.80	0.30	12.48	
	cross(W0227)								
	0-30	2	30.00			0.80	0.30	14.40	
	30-36	2	6.00			0.80	0.30	2.88	
					Total Qty Work Done			866.22	Sqm
					Qty Payable in this bill			866.22	Sqm

Contractor Representative

Assistant Engineer

Asst.Executive Engineer
ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಟಿ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಜಿ.ಜಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No 15..

Measurement Sheet

First and Final

Item No: 3

Item Name: KSRRB M2100-10. Providing and laying Plain cement concrete of mix 1:3:6 with OPC @ 220kgs, with crushed 40mm and down size graded granite metal coarse aggregates @0.89cum and fine aggregates @ 0.46cum, in foundation mechanically mixed, placed in foundation and compacted by vibration including curing for 14 days including cost of all materials, labour, HOM curing, form works, scaffolding and centering complete as per specifications. MORTH Specification No. 2100 (P.222/I.27.18) PWD - SR 2018-19)

CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	1	30.00			0.90	0.15	4.05	
30-60	1	30.00			0.90	0.15	4.05	
60-90	1	30.00			0.90	0.15	4.05	
90-110	1	20.00			0.90	0.15	2.70	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			0.90	0.15	4.05	
30-60	1	30.00			0.90	0.15	4.05	
60-90	1	30.00			0.90	0.15	4.05	
90-120	1	30.00			0.90	0.15	4.05	
120-138	1	18.00			0.90	0.15	2.43	
1st cross(W0214)								
0-30	2	30.00			0.90	0.10	5.40	
30-60	2	30.00			0.90	0.10	5.40	
60-85	2	25.00			0.90	0.10	4.50	
2nd cross((W0212)								
0-30	2	30.00			0.90	0.10	5.40	
30-60	2	30.00			0.90	0.10	5.40	
60-90	2	30.00			0.90	0.10	5.40	
90-116	2	26.00			0.90	0.10	4.68	
cross(W0227)								
0-30	2	30.00			0.90	0.10	5.40	
30-36	2	6.00			0.90	0.10	1.08	
cross(W0229)								
0-30	2	30.00			0.90	0.10	5.40	
30-38	2	8.00			0.90	0.10	1.44	
road side and kerb								
0-100	1	100.00			0.30	0.10	3.00	
100-200	1	100.00			0.30	0.10	3.00	
200-248	1	48.00			0.30	0.10	1.44	
						Total Qty Work Done	90.42	**cum**
						Qty Payable in this bill	90.42	**Cum**

Contractor Representative

Assistant Engineer

Asst.Executive Engineer

ಬಿ.ಬಿ.ಎಂ.ಪಿ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಪೂರ್ವ ವಿಭಾಗ
ಬಿ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet

First and Final

Item No: 4

Item Name: KSRB 4-1.6 ; Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.69 cum and fine aggregtes @ 0.459cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, ncluding cost of all materials, labour, HOM of machinery, curing complete as per specifications. Specification No. KBS 4.1, 4.2. (P.No.13, I.No. 4.6 of PWD SR 2018-19)

	CHAINAGE Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
	Bharathi Theater(W0223)								
	0-30	2	30.00			0.15	0.80	7.20	
	30-60	2	30.00			0.15	0.80	7.20	
	60-90	2	30.00			0.15	0.80	7.20	
	90-110	2	20.00			0.15	0.80	4.80	
	Excel kalyana mantapa(W0225)								
	0-30	2	30.00			0.15	0.80	7.20	
	30-60	2	30.00			0.15	0.80	7.20	
	60-90	2	30.00			0.15	0.80	7.20	
	90-120	2	30.00			0.15	0.80	7.20	
	120-138	2	18.00			0.15	0.80	4.32	
	1st cross(W0214)								
	0-30	4	30.00			0.15	0.60	10.80	
	30-60	4	30.00			0.15	0.60	10.80	
	60-85	4	25.00			0.15	0.60	9.00	
	2nd cross((W0212)								
	0-30	4	30.00			0.15	0.60	10.80	
	30-60	4	30.00			0.15	0.60	10.80	
	60-90	4	30.00			0.15	0.60	10.80	
	90-116	4	26.00			0.15	0.60	9.36	
	cross(W0227)								
	0-30	4	30.00			0.15	0.20	3.60	
	30-36	4	6.00			0.15	0.20	0.72	
	cross(W0229)								
	0-30	4	30.00			0.15	0.20	3.60	
	30-38	4	8.00			0.15	0.20	0.96	
							Total Qty Work Done	**140.76**	**Cum**
							Qty Payable in this bill	**140.76**	**Cum**

Contractor Representative

Assistant Engineer

18/12

Asst.Executive Engineer

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು

ಜ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ

ಬಾಗಲಗುಂಟೆ, ಬಿ.ಬಿ.ಎಂ.ಪಿ

ಬೆಂಗಳೂರು-560073

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet

First and Final

Item No:	5
Item Name:	Providing and fixing RCC precast Slabs of 0.10 m thick of CC M20 with 20 mm and down size graded granite metal , machine mixed , including cost of all material , labour , HOM of Machinery , curing complete

	CHAINAGE Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
	Bharathi Theater(W0223)								
	0-30	1	30.00			0.90		27.00	
	30-60	1	30.00			0.90		27.00	
	60-90	1	30.00			0.90		27.00	
	90-102	1	12.00			0.90		10.80	
	Excel kalyana mantapa(W0225)								
	0-30	1	30.00			0.90		27.00	
	30-60	1	30.00			0.90		27.00	
	60-90	1	30.00			0.90		27.00	
	90-120	1	30.00			0.90		27.00	
	120-138	1	18.00			0.90		16.20	
	1st cross(W0214)								
	0-30	2	30.00			0.90		54.00	
	30-60	2	30.00			0.90		54.00	
	60-85	2	25.00			0.90		45.00	
	2nd cross (W0212)								
	0-30	2	30.00			0.90		54.00	
	30-52	2	22.00			0.90		39.60	
							Total Qty Work Done	462.60	Cum
							Qty Payable in this bill	460.00	Cum

Contractor Representative

Assistant Engineer

Asst.Executive Engineer
ಉ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet

First and Final

Item No:	6
Item Name:	Providing and fixing Pre cast solid concrete kerb stones made out of No.272.21 CC 1:2:4 and finished with CM 1:3 plastering and finishing cutting etc. complete -do- of size 450x200x400 mm PWD SR 2018-19 (P-27, I No-5.29.1)

	CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
	Bharathi Theater(W0223)								
	0-30	1	30.00					30.00	
	30-60	1	30.00					30.00	
	60-90	1	30.00					30.00	
	90-110	1	20.00					20.00	
	Excel kalyana mantapa(W0225)								
	0-30	1	30.00					30.00	
	30-60	1	30.00					30.00	
	60-90	1	30.00					30.00	
	90-120	1	30.00					30.00	
	120-138	1	18.00					18.00	
							Total Qty Work Done	248.00	
							No of Kerbs length /0.45=	551.11	
							Qty Payable in this bill	551.11	No

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಐ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Contractor Representative

Assistant Engineer
28/1

Asst.Executive Engineer ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಐ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet

First and Final

Item No: 7

Item Name: KSRB 15-19.1 : Providing and applying ready mix priming coat over concrete / masonry / asbestos cement sheet / plastered surfaces including preparing the surface after thoroughly cleaning of oil, grease, dirt and other foreign matter, and sand papering including cost of materials, labour, complete as per specifications SR 2018-19 P 124 I 15.80

	CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
	Bharathi Theater(W0223)								
	0-30	1	30.00				0.35	10.50	
	30-60	1	30.00				0.35	10.50	
	60-90	1	30.00				0.35	10.50	
	90-110	1	20.00				0.35	7.00	
	Excel kalyana mantapa(W0225)								
	0-30	1	30.00				0.35	10.50	
	30-60	1	30.00				0.35	10.50	
	60-90	1	30.00				0.35	10.50	
	90-120	1	30.00				0.35	10.50	
	120-138	1	18.00				0.35	6.30	
							Total Qty Work Done	86.80	Sqm
							Qty Payable in this bill	86.80	Sqm

48.30

Contractor Representative

Assistant Engineer 15/2

Asst.Executive Engineer
ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರ
ಟಿ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಜಿ.ಜಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-56007

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet

First and Final

Item No:	8
Item Name:	KSRB 15-19.2 : Providing and applying spray painting in two coats (excluding priming coat) over concrete / masonry / asbestos cement sheet / plastered surfaces with flat wall paint of approved brand to give even shade after cleaning the surface of all dirt, dust and other foreign matter, and sand papering including cost of materials, labour, complete as per specifications.SR 2018-19 P 124 I 15.81

	CHAINAGE Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
	Bharathi Theater(W0223)								
	0-30	1	30.00				0.35	10.50	
	30-60	1	30.00				0.35	10.50	
	60-90	1	30.00				0.35	10.50	
	90-110	1	20.00				0.35	7.00	
	Excel kalyana mantapa(W0225)								
	0-30	1	30.00				0.35	10.50	
	30-60	1	30.00				0.35	10.50	
	60-90	1	30.00				0.35	10.50	
	90-120	1	30.00				0.35	10.50	
	120-138	1	18.00				0.35	6.30	
							Total Qty Work Done	**86.80**	**Sqm**
							Qty Payable in this bill	**86.80**	**Sqm**

48.30

Contractor Representative

Assistant Engineer 15/2

Asst.Executive Engineer

ಉ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ

ಬಾಗಲಗುಂಟೆ. ಜಿ.ಜಿ.ಎಂ.ಪಿ

ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet

First and Final

Item No: 9

Item Name: Providing and SUPPLYING Stone Dust/Grit,4.75mmto0.075.SR 2108-19 P II I0400

	CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
	Bharathi Theater(W0223)								
	0-30	1	30.00			7.60	0.10	22.80	
	30-60	1	30.00			7.40	0.10	22.20	
	60-90	1	30.00			7.20	0.10	21.60	
	90-110	1	20.00			6.90	0.10	13.80	
	Excel kalyana mantapa(W0225)								
	0-30	1	30.00			3.80	0.10	11.40	
	30-60	1	30.00			3.80	0.10	11.40	
	60-90	1	30.00			3.80	0.10	11.40	
	90-120	1	30.00			3.60	0.10	10.80	
	120-138	1	18.00			3.80	0.10	6.84	
						Total Qty Work Done		**132.24**	**Cum**
						Qty Payable in this bill		**132.05**	**Cum**

Contractor Representative

Assistant Engineer 2/2

Asst.Executive Engineer

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಆ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾ.ಮ.ಗುಂ.ಪಾ. ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು 56007

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No 15..

Measurement Sheet

First and Final

Item No.	10
Item Name:	KSRRB M400-6.2. Construction of granular sub-base by providing close graded crushed stone aggregates of granite / trap / basalt material, spreading in uniform layers with motor grader on prepared surface, mixingby mix in place method by rotavator at OMC, and compacting with vibratory power roller to achieve the desired density, complete as per specifications. B. By Mix in Place Method. - For Grading II Material SR2018-19 P 153, I 20.6

CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	1	30.00			7.60	0.15	34.20	
30-60	1	30.00			7.40	0.15	33.30	
60-90	1	30.00			7.20	0.15	32.40	
90-110	1	20.00			6.90	0.15	20.70	
Total Qty Work Done							**120.60**	**Cum**
Qty Payable in this bill							**120.45**	**Cum**

Contractor Representative

Assistant Engineer 2/2

Asst.Executive Engineer
ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ದಾ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-56007

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No 15..

Measurement Sheet

First and Final

Item No:	11
Item Name:	KSRRB M400- Wet Mix Macadam KSRRB M400-17. Providing, laying, spreading and compacting crushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed method of tipper to site, laying in uniform layers with paver in sub-base/base course on well prepared surface and compacting with vibratory roller to achieve the desired density complete as per specifications. MORTH Specification No. 406SR RATE 2018-19,P 155 I 20.18

CHAINAGE Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	1	30.00			7.60	0.10	22.80	
30-60	1	30.00			7.40	0.10	22.20	
60-90	1	30.00			7.20	0.10	21.60	
90-110	1	20.00			6.90	0.10	13.80	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			3.80	0.10	11.40	
30-60	1	30.00			3.80	0.10	11.40	
60-90	1	30.00			3.80	0.15	17.10	
90-120	1	30.00			3.80	0.10	11.40	
120-138	1	18.00			3.80	0.15	10.26	
1st cross(W0214)								
0-30	1	30.00			1.20	0.10	3.60	
30-60	1	30.00			1.20	0.10	3.60	
60-85	1	25.00			1.20	0.10	3.00	
2nd cross((W0212)								
0-30	1	30.00			1.20	0.10	3.60	
30-60	1	30.00			1.20	0.10	3.60	
60-90	1	30.00			1.20	0.10	3.60	
90-116	1	26.00			1.20	0.10	3.12	
cross(W0227)								
0-30	1	30.00			1.20	0.10	3.60	
30-36	1	6.00			1.20	0.10	0.72	
cross(W0229)								
0-30	1	30.00			1.20	0.10	3.60	
30-38	1	8.00			1.20	0.10	0.96	
						Total Qty Work Done	**174.96**	**mtr**
						Qty Payable in this bill	**172.43**	**mtr**

Contractor Representative

Assistant Engineer 8/2

Asst.Executive Engineer
ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet

First and Final

Item No: **12**

Item Name: KSRRB M500-6. Providing and applying primer coat with S.S. bitumen emulsion on prepared surface of granular base such as WMM including cleaning of road surface and spraying primer at the rate of 0.60 kg / sqm using mechanical means complete as per specifications. MORTH Specification No. 502 SR 2018-19 P158 il 21.6

CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	1	30.00			7.60		228.00	
30-60	1	30.00			7.40		222.00	
60-90	1	30.00			7.20		216.00	
90-110	1	20.00			6.90		138.00	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			3.40		102.00	
30-60	1	30.00			3.40		102.00	
60-90	1	30.00			3.40		102.00	
90-120	1	30.00			3.40		102.00	
120-138	1	18.00			3.40		61.20	
						Total Qty Work Done	**1273.20**	**Sqm**
						Qty Payable in this bill	**1272.20**	**Sqm**

Contractor Representative

Assistant Engineer 12/2

Asst.Executive Engineer
ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಧಿಯಂತರರು
ಡಿ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet

First and Final

Item No: 13

Item Name: KSRRB M500-17. Providing and laying dense graded bituminous macadam using crushed aggregates of specified grading, premixed with VG30 grade bituminous binder and, transporting the hot mix to work site, laying to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction as per MORTH table 500-10 complete in all respects complete as per specifications.. MORTH Specification No. 507 - using 40/60 TPH capacity H.M.P. with Mechanical paver Gr-II (50 mm to 75 mm) with 4.5 % VG-30 Bitumen. SR 2018-19.P160,I 21.17.6

CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	1	30.00			7.60	0.05	11.40	
30-60	1	30.00			7.40	0.05	11.10	
60-90	1	30.00			7.20	0.05	10.80	
90-110	1	20.00			6.90	0.05	6.90	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			3.80	0.05	5.70	
30-60	1	30.00			3.40	0.05	5.10	
60-90	1	30.00			3.80	0.05	5.70	
90-120	1	30.00			3.60	0.05	5.40	
120-138	1	18.00			3.80	0.05	3.42	
1st cross(W0214)								
0-30	1	30.00			1.20	0.05	1.80	
30-60	1	30.00			1.20	0.05	1.80	
60-85	1	25.00			1.20	0.05	1.50	
2nd cross((W0212)								
0-30	1	30.00			1.20	0.05	1.80	
30-60	1	30.00			1.20	0.05	1.80	
60-90	1	30.00			1.20	0.05	1.80	
90-116	1	26.00			1.20	0.05	1.56	
cross(W0227)								
0-30	1	30.00			1.20	0.05	1.80	
30-36	1	6.00			1.20	0.05	0.36	
cross(W0229)								
0-30	1	30.00			1.20	0.05	1.80	
30-38	1	8.00			1.20	0.05	0.48	
							82.02	

Scanned with CamScanner

CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
road Profile correction for road								
Bharathi Theater(W0223)								
0-30	1	30.00			7.60		228.00	
30-60	1	30.00			7.40		222.00	
60-90	1	30.00			7.20		216.00	
90-110	1	20.00			6.90		138.00	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			7.30		219.00	
30-60	1	30.00			7.40		222.00	
60-90	1	30.00			7.30		219.00	
90-120	1	30.00			7.20		216.00	
120-138	1	18.00			7.30		131.40	
1st cross(W0214)								
0-30	1	30.00			4.50		135.00	
30-60	1	30.00			4.50		135.00	
60-85	1	25.00			4.50		112.50	
2nd cross((W0212)								
0-30	1	30.00			5.30		159.00	
30-60	1	30.00			5.40		162.00	
60-90	1	30.00			5.20		156.00	
90-116	1	26.00			5.30		137.80	
cross(W0227)								
0-30	1	30.00			5.40		162.00	
30-36	1	6.00			5.40		32.40	
cross(W0229)								
0-30	1	30.00			5.40		162.00	
30-38	1	8.00			5.40		43.20	
							3208.30	
road Profile correction for road							64.17	
Total Qty Work Done							**146.19**	**cum**
Qty Payable in this bill							**145.53**	**Cum**

Contractor Representative

Assistant Engineer 12/2

Asst.Executive Engineer
ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಜಿ.ಜಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet

First and Final

Item No: 14

Item Name: KSRRB M500-10. Providing and applying tack coat using 80/100 grade bitumen(VG10) in boiler fitted with spray set distributor at the rate of 0.20 kg per sqm on the existing prepared bituminous surface cleaned with mchancial broom. complete as per specifications. - using bitumen 80/100 on primed surfaces SR2018-19,P159,I 21.10

CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	1	30.00			7.60		228.00	
30-60	1	30.00			7.40		222.00	
60-90	1	30.00			7.20		216.00	
90-110	1	20.00			6.90		138.00	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			7.30		219.00	
30-60	1	30.00			7.30		219.00	
60-90	1	30.00			7.30		219.00	
90-120	1	30.00			7.30		219.00	
120-138	1	18.00			7.30		131.40	
1st cross(W0214)								
0-30	1	30.00			4.50		135.00	
30-60	1	30.00			4.50		135.00	
60-85	1	25.00			4.50		112.50	
2nd cross((W0212)								
0-30	1	30.00			5.30		159.00	
30-60	1	30.00			5.30		159.00	
60-90	1	30.00			5.30		159.00	
90-116	1	26.00			5.30		137.80	
cross(W0227)								
0-30	1	30.00			5.40		162.00	
30-36	1	6.00			5.40		32.40	
cross(W0229)								
0-30	1	30.00			5.40		162.00	
30-38	1	8.00			5.40		43.20	
						Total Qty Work Done	**3208.30**	**Sqm**
						Qty Payable in this bill	**3207.30**	**Sqm**

Contractor Representative

Assistant Engineer 12/2

Asst.Executive Engineer

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಜ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬೆ.ಬ
ಬೆಂಗಳೂರು 57

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No 15..

Measurement Sheet
First and Final

Item No: **15**

Item Name: Providing and laying Bituminous concrete 40mm thick with hot mix plant, using crushed aggregates of specified grading, premixed with bituminous binder and filler, transporting the hot mix to work site, laying with a paver finisher to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction in all respects complete as per specifications. Clause 507 of MORTH V Revision as per IRC SP-53-2015 using 40-60 TPH capacity HMP with mechanical paver grading II Cum (30-45mm) with 5.4 % of modified bituminous binder consisting of 4.97% of VG-30 bitumen (60/70 grade) and 0.43% of plastomeric thermoplastics (waste plastic) (p-171, lt 21.78.12) PWD SR 2018-19)

CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	1	30.00			7.60	0.04	9.12	
30-60	1	30.00			7.40	0.04	8.88	
60-90	1	30.00			7.20	0.04	8.64	
90-110	1	20.00			6.90	0.04	5.52	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			7.30	0.04	8.76	
30-60	1	30.00			7.30	0.04	8.76	
60-90	1	30.00			7.30	0.04	8.76	
90-120	1	30.00			7.30	0.04	8.76	
120-138	1	18.00			7.30	0.04	5.26	
1st cross(W0214)								
0-30	1	30.00			4.50	0.04	5.40	
30-60	1	30.00			4.50	0.04	5.40	
60-85	1	25.00			4.50	0.04	4.50	
2nd cross((W0212)								
0-30	1	30.00			5.30	0.04	6.36	
30-60	1	30.00			5.30	0.04	6.36	
60-90	1	30.00			5.30	0.04	6.36	
90-116	1	26.00			5.30	0.04	5.51	
cross(W0227)								
0-30	1	30.00			5.40	0.04	6.48	
30-36	1	6.00			5.40	0.04	1.30	
cross(W0229)								
0-30	1	30.00			5.40	0.04	6.48	
30-38	1	8.00			5.40	0.04	1.73	
						Total Qty Work Done	**128.33**	**Cum**
						Qty Payable in this bill	**128.29**	**Cum**

D. Murthy
Contractor Representative

Assistant Engineer
15/2

Asst.Executive Engineer
ಪಾಲಿಕೆ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಐ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಜಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು-560073

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No

Measurement Sheet
First and Final

Item No:	16
Item Name:	KSRRB M800-13.Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bitumin ous Surface:- Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads at 250 gms per sqm area, thickness of 2.5 mm is exclusive of surface applied glass beads as per IRC:35. The finished surface to be level, uniform and free from streaks and holes complete as per specifications. MORTH Specification No. 803 SR2018-19,P 182 I 24.15

CHAINAGE Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	2	30.00			0.10		6.00	
30-60	2	30.00			0.10		6.00	
60-90	2	30.00			0.10		6.00	
90-110	2	20.00			0.10		4.00	
Excel kalyana mantapa(W0225)								
0-30	2	30.00			0.10		6.00	
30-60	2	30.00			0.10		6.00	
60-90	2	30.00			0.10		6.00	
90-120	2	30.00			0.10		6.00	
120-138	2	18.00			0.10		3.60	
1st cross(W0214)								
0-30	2	30.00			0.10		6.00	
30-60	2	30.00			0.10		6.00	
60-85	2	25.00			0.10		5.00	
2nd cross((W0212)								
0-30	2	30.00			0.10		6.00	
30-60	2	30.00			0.10		6.00	
60-90	2	30.00			0.10		6.00	
90-116	2	26.00			0.10		5.20	
cross(W0227)								
0-30	2	30.00			0.10		6.00	
30-36	2	6.00			0.10		1.20	
cross(W0229)								
0-30	2	30.00			0.10		6.00	
30-38	2	8.00			0.10		1.60	
						Total Qty Work Done	**104.60**	**Sqm**
						Qty Payable in this bill	**104.60**	**Sqm**

Contractor Representative

Assistant Engineer 15/2

Asst.Executive Engineer
ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಪೂ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಪಿ.ಬಿ.ಎಂ.ಸಿ
ಬೆಂಗಳೂರು ಕ

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements of CC Drain and Covering Slab and RE-Asphalting Excel Kalyana Mantapa road and Bharathi Theater roads in Dasarahalli Ward No 15..

Measurement Sheet

First and Final

Item No: **17**

Item Name: KSRRB M100-1 Loading and unloading of stone boulder/stone aggregates/sand/.kanker/moorum. KSRRB M100-1:Placing tipper at loading point, loading with front end loader, dumping, turning for return trip, excluding time for haulage and return trip complete as per specification MORTH Chapter 1 PWD SR 2018-19 (P-136, It.No. 17.1)

CHAINAGE / Land Mark	NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
Bharathi Theater(W0223)								
0-30	1	30.00			0.90	1.20	32.40	
30-60	1	30.00			0.90	1.20	32.40	
60-90	1	30.00			0.90	1.20	32.40	
90-116	1	26.00			0.90	1.20	28.08	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			0.90	1.20	32.40	
30-60	1	30.00			0.90	1.20	32.40	
60-90	1	30.00			0.90	1.20	32.40	
90-120	1	30.00			0.90	1.20	32.40	
120-138	1	18.00			0.90	1.20	19.44	
1st cross(W0214)								
0-30	2	30.00			0.90	0.75	40.50	
30-60	2	30.00			0.90	0.75	40.50	
60-85	2	25.00			0.90	0.75	33.75	
2nd cross((W0212)								
0-30	2	30.00			0.90	0.75	40.50	
30-60	2	30.00			0.90	0.75	40.50	
60-90	2	30.00			0.90	0.75	40.50	
90-116	2	26.00			0.90	0.75	35.10	
cross(W0227)								
0-30	2	30.00			0.90	0.75	40.50	
30-36	2	6.00			0.90	0.75	8.10	
cross(W0229)								
0-30	2	30.00			0.90	0.75	40.50	
30-38	2	8.00			0.90	0.75	10.80	
Bharathi Theater(W0223)								
0-30	1	30.00			7.60	0.40	91.20	
30-60	1	30.00			7.40	0.40	88.80	
60-75	1	15.00			7.10	0.30	31.95	
Excel kalyana mantapa(W0225)								
0-30	1	30.00			3.80	1.20	136.80	
30-48	1	18.00			3.90	1.20	84.24	
						Total Qty Work Done	**1078.56**	**Cum**
						Qty Payable in this bill	**1072.00**	**Cum**

Contractor Representative

Assistant Engineer

18/1

Asst.Executive Engineer

ಸಹಾಯಕ ಕಾರ್ಯ ನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಐ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ. ಬಿ.ಬಿ.ಎಂ.ಪಿ
ಬೆಂಗಳೂರು 5[illegible]

Scanned with CamScanner

Name of work:- Improvements of CC drain & Covering Slab and Re-asphalting Excal Kalyana mantapa Road & Bharathi theatre Roads in Dasarahalli Ward No-15.

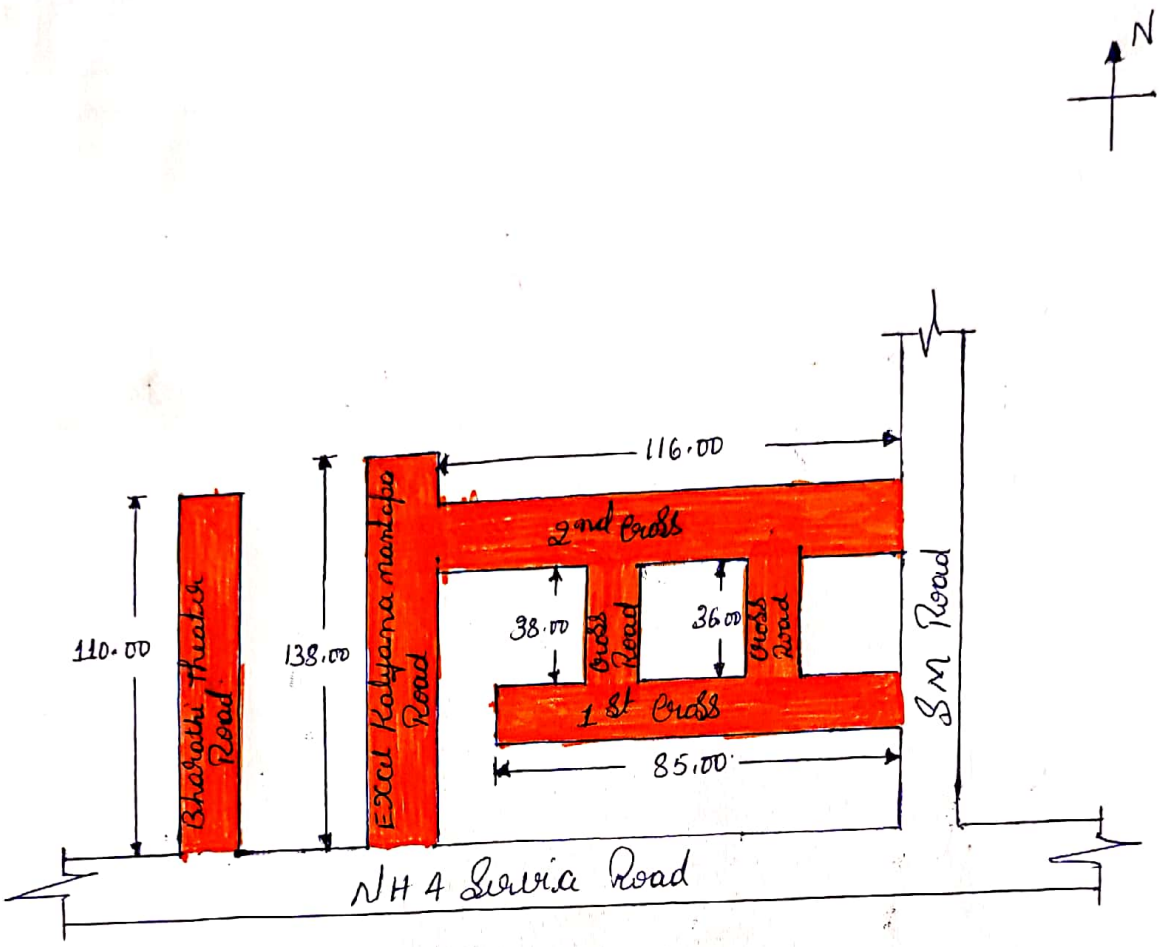

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು.
ಜಿ. ದಾಸರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಾ:ಗುಂಟೆ. ಜಿ.ಜಿ.ಎಂ.ಪಿ
ಂಗಳೂರು 5600

Scanned with CamScanner
